



Amber Bell <amberbell000@gmail.com>

Fwd: Repair Estimate - 3414 S Belcher Dr

2 messages

Erik Devlin <e1devlin@hotmail.com>
To: Amber Bell <amberbell000@gmail.com>

Tue, Oct 29, 2024 at 11:56 AM

Sent from my iPhone

Begin forwarded message:

From: MICHAL WINIAREK <mikew@llwbuild.com>
Date: October 29, 2024 at 10:15:13 AM EDT
To: e1devlin@hotmail.com
Subject: Repair Estimate - 3414 S Belcher Dr

Hi Erik

Attached is the exact image estimate to repair your home on Belcher. Please take a look and let me know if you have any questions .

Thanks

Mike

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: info@estimate-experts.com <info@estimate-experts.com>
Sent: Tuesday, October 29, 2024 9:33:38 AM
To: MICHAL WINIAREK <mikew@llwbuild.com>
Subject: Michal here is your Erik Devlin - 3414 S Belcher Dr Tampa, FL 33629, USA - Buildback estimate

Hi Michal,

Attached to this email you will find the requested estimate. Please take a look and let us know if anything needs to be changed or adjusted. We are always happy to make modifications that better suit your needs and preferences.

If there are any questions or concerns about the estimate, please do not hesitate to contact us directly at our office. We look forward to hearing from you soon!

Regards,
Estimate Experts Team
+1 (561) 677-2977
info@estimate-experts.com

 **3414SBELCHERDR-BB-102424.pdf**
454K

Erik Devlin <e1devlin@hotmail.com>
To: Amber Bell <amberbell000@gmail.com>

Fri, Nov 8, 2024 at 2:45 PM

Cc: Michal Winiarek <mikew@llwbuild.com>

Hey Mike,

Looking to move forward. Whats the next step? Contract ? If you could send us something that would be greatly appreciated.

Have a good weekend !

Erik Devlin
Sent from my iPhone

On Oct 29, 2024, at 11:56 AM, Erik Devlin <e1devlin@hotmail.com> wrote:

[Quoted text hidden]

<3414SBELCHERDR-BB-102424.pdf>



Amber Bell <amberbell000@gmail.com>

Fwd: Contract - 3414 Belcher

2 messages

Erik Devlin <e1devlin@hotmail.com>
To: Amber Bell <amberbell000@gmail.com>

Mon, Nov 11, 2024 at 6:11 PM

Sent from my iPhone

Begin forwarded message:

From: MICHAL WINIAREK <mikew@llwbuild.com>
Date: November 11, 2024 at 4:34:04 PM EST
To: Erik Devlin <e1devlin@hotmail.com>
Subject: Contract - 3414 Belcher

Hi Erik,

Attached is the contract for the work on your home. Please review and let me know if you have any questions.

We have a few items that are considered Allowances (there is a page in the contract that specifies these), and since these items are heavily dependent on your material choices, we set an amount that is included in the contract for such items.

Depending on what cabinet package you end up choosing, the entire project should not take longer than 4-6 weeks. (it may be a little longer if we encounter longer lead times for the material)

If all looks ok, then let me know and I will send over a DocuSign. Please send me Amber's email as well (I used her name as on the public records).

Thanks,

Mike.

Michal J. Winiarek

Certified Building Contractor

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com

2 attachments



Contract for Construction - 3414 Belcher.pdf
738K

Erik Devlin <e1devlin@hotmail.com>
To: Amir Ghaeenezadeh <amir@amethystlawgroup.com>
Cc: Amber Bell <amberbell000@gmail.com>

Tue, Nov 12, 2024 at 10:34 AM

Amir,

Hello attached is a contract to get our home
Rebuilt from the hurricane.

Thoughts ??

Erik Devlin

Sent from my iPhone

Begin forwarded message:

From: Erik Devlin <e1devlin@hotmail.com>
Date: November 11, 2024 at 6:11:08 PM EST
To: Amber Bell <amberbell000@gmail.com>
Subject: Fwd: Contract - 3414 Belcher

[Quoted text hidden]

2 attachments





Contract for Construction - 3414 Belcher.pdf
738K



Amber Bell <amberbell000@gmail.com>

Cabinets

2 messages

MICHAL WINIAREK <mikew@llwbuild.com>

Wed, Dec 11, 2024 at 11:07 AM

To: Erik Devlin <e1devlin@hotmail.com>, Amber Bell <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>

Hi Erik and Amber,

Attached is some information regarding the cabinet package for the kitchen. Please let me know if this looks OK. I can have them here in about a week to 10 days.

Thanks,

Mike.

Michal J. Winiarek

Certified Building Contractor



Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com

3 attachments

 **Bright White Shaker.pdf**
239K

 **Gray Shaker.pdf**
286K

 **Belcher Kitchen Project V1.pdf**
3342K

Amber Bell <amberbell000@gmail.com>
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Erik Devlin <e1devlin@hotmail.com>, Sharon Knight <sharonk@llwbuild.com>

Wed, Dec 11, 2024 at 11:16 AM

Hi Mike,

Looks exactly like what we had and good to me. I'll let Erik confirm.

Thanks,

Amber

On Dec 11, 2024, at 11:07 AM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik and Amber,

Attached is some information regarding the cabinet package for the kitchen. Please let me know if this looks OK. I can have them here in about a week to 10 days.

Thanks,

Mike.

Michal J. Winiarek

Certified Building Contractor

<image001.jpg>

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com

<Bright White Shaker.pdf>

<Gray Shaker.pdf>

<Belcher Kitchen Project V1.pdf>



Amber Bell <amberbell000@gmail.com>

Plan to Completion - Belcher

1 message

MICHAL WINIAREK <mikew@llwbuild.com>

Fri, Jan 10, 2025 at 6:10 PM

To: Erik Devlin <e1devlin@hotmail.com>, Amber Bell <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>

Hi Erik and Amber,

We just revised the project schedule and here is what we can expect moving forward:

- Walls corrected and primed; stone picked up; plumbing modifications completed; tile prep and backer board installed by 1/17
- Doors and trim installed; paint 1 completed by 1/28
- Tile installed and cabinets delivered by 2/7
- Cabinets and counters installed; locks, hardware, shelving installed by 2/14
- Backsplashes installed; trim plumbing and electric completed; final clean performed by 2/20
- Home Delivery 2/21

The above is a condensed plan – we have a much more detailed project schedule that we manage internally. Thank you for being patient so far.

Have great weekend.

Mike.

Michal J. Winiarek

Certified Building Contractor



LLW Construction, Inc.

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com



Amber Bell <amberbell000@gmail.com>

Fwd: Delvin – Selections

2 messages

Sharon Knight <sharonk@llwbuild.com>
To: "amberbell000@gmail.com" <amberbell000@gmail.com>

Sat, Jan 18, 2025 at 11:40 AM

Please see attached list of materials to be selected.

You can look through www.build.com, and I recommend H depot re: front door.
Lowe's for cabinet/door hardware.
Send me what you like and let me know if you have any questions.

Thanks!
Sharon

Get [Outlook for iOS](#)

 **Selections .pdf**
27K

Amber Bell <amberbell000@gmail.com>
To: Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Thu, Jan 23, 2025 at 4:02 PM

Sharon,

Please see selections for reference attached. As discussed, I don't know what I'm doing so I've picked the look that I like best. If you can find other options for less, please let me know.

Appliances: We want to stick with Kitchen Aid and prefer the water/ice to be on the refrigerator door. The pictures I've included are out of budget but look like what we had before with the exception of the fridge which now includes the water/ice option. I'm hoping you can get better "builder" pricing somewhere. Let's discuss before you order.

Master Bath: We are going to use the hand held shower w/ slider bar, shower head & arm, and trim we previously had.

Bathroom #2: I've chosen something other than Delta Fixtures and based on our conversation that shouldn't be an issue. I know the shower fixtures come with a tub connection that we don't need, but it was cheaper than the other options I was seeing. If you can find something with the same aesthetic for less, or that makes more sense, please send me a picture and I'll take a look.

Doors: I spoke to Erik and we are good with hollow interior doors. As mentioned, I prefer single or double panel in lieu of 6 panel if we can get those in our budget. Also, in pricing front doors, fiberglass is really expensive. Can we do steel? If so, what are the pros and cons to both? We are going to use all the cabinet and door hardware we previously had, including the front door.

Hallway Bathroom: I would like to have another conversation with you about this. Please give me a call when you have a sec to chat.

Thank you,

Amber Bell
813.335.9891

[Quoted text hidden]



Belcher Finishes - LLW.pdf
890K



Amber Bell <amberbell000@gmail.com>

Phone has been off for two days

1 message

Erik Devlin <e1devlin@hotmail.com>

Tue, Feb 4, 2025 at 1:46 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Hey Mike,

Hope you are ok. I text yesterday and today as well as called yesterday and today. Goes right to voicemail looks like your phone is in Do not disturb.

Please let me know you are good

Thanks !!

Erik

Sent from my iPhone

On Jan 10, 2025, at 6:10 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik and Amber,

We just revised the project schedule and here is what we can expect moving forward:

- Walls corrected and primed; stone picked up; plumbing modifications completed; tile prep and backer board installed by 1/17
- Doors and trim installed; paint 1 completed by 1/28
- Tile installed and cabinets delivered by 2/7
- Cabinets and counters installed; locks, hardware, shelving installed by 2/14
- Backsplashes installed; trim plumbing and electric completed; final clean performed by 2/20
- Home Delivery 2/21

The above is a condensed plan – we have a much more detailed project schedule that we manage internally. Thank you for being patient so far.

Have great weekend.

Mike.

Michal J. Winiarek

Certified Building Contractor

<image001.jpg>

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com





Amber Bell <amberbell000@gmail.com>

Re: Communications

2 messages

Erik Devlin <e1devlin@hotmail.com>

Sun, Feb 16, 2025 at 8:56 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Our text thread last week we asked for updates Monday and Tuesday. You said you would have an update Tuesday and you did not update us as you said you would. Wednesday we reached out again asking for updates. You said cabinets Friday or Monday.

We had questions to that reply. Do floors need to go before cabinets ? Again nothing. I called you Wednesday and Thursday and texted you individually asking for a call.

So when you ask if you are on call this weekend, you tell me . Did you take care of what you needed to last week?

I expect if we email call or text Monday-Friday that you respond to us that day.

Also you gave us a timeline.

You initially said 4-6 weeks after we signed the contract, from the time you started until finished. We had expectations based on that timeline. Latest timeline says February 21st. So where are we? No bathrooms, cabinets or floors done to date.

We need accountability with the timelines that are given. Otherwise we want answers and updates of why things are not getting done and what you're planning to do to stay on track.

Our monthly expenses are twice what they normally are every month we're not back in our home. Stop with excuses and lets get moving forward.

Calling, texting, emailing tomorrow to get an update.

Sent from my iPhone

On Feb 16, 2025, at 4:38 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

I'm sorry Erik - it was on do not disturb today as I was at my sons rowing regatta yesterday and today. I video all their races and if a call comes in, the video stops. I did not expect to be on call this weekend. Was it an emergency?

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Sunday, February 16, 2025 1:27:23 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>; Sharon Knight <sharonk@llwbuild.com>

Subject: Communications

Hey Mike,

Phone is on "do not disturb" again. We chatted about this once before, can we expect This moving forward ?

A time line of February 21st was given by you to us . We are trying to follow up on the time Line here.

If that is not accurate please give us accurate time line instead of false hope. It would be better for all of us.

Any recommendations on what to do here ?

If you were in our shoes what would you do ?

Help me help you .

I have got some floor guys on standby if ya need help also have HVAC guys too.

Ya got to talk to me fella

Thanks !

Erik

Sent from my iPhone

MICHAL WINIAREK <mikew@llwbuild.com>

To: Erik Devlin <e1devlin@hotmail.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Mon, Feb 17, 2025 at 9:34 AM

Ok. - let me get a handle on it and I'll reach out later today.

Mike

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Sunday, February 16, 2025 8:56:36 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>; Sharon Knight <sharonk@llwbuild.com>

Subject: Re: Communications

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Belcher Dr - Update 2.17.25

2 messages

MICHAL WINIAREK <mikew@llwbuild.com>

Mon, Feb 17, 2025 at 5:25 PM

To: Erik Devlin <e1devlin@hotmail.com>, "amberbell000@gmail.com" <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>

Hi Erik and Amber,

Here is a brief update for your project on Belcher Dr:

- We received a cabinet shipment for your white kitchen cabinets today – we have them in our storage until we are ready to install.
- The tile installer is ready to begin the tile work, starting with the floor prep tomorrow – it should take a maximum of 3-4 days of prep.
 - We are getting prep materials to the site tonight or tomorrow first thing.
 - The contents that are in the way will be moved to one of the bedrooms – our men will do it first thing in the morning. They will relocate as needed.
- The plumbers will issue a proposal for the master bath plumbing modifications per your conversation with them.
- Shower pan liners, plumbing, and drains installation is completed.
 - Ready for mud bed and tile backer.
- We are ready to hang interior doors – will do this either after the floor prep is complete or after the main floor tile is installed, whichever order keeps things moving faster.

That is all we have today. This should take us through the next 7-10 days. I will submit additional information later in the week as we receive it.

Thanks,

Mike

Michal J. Winiarek

Certified Building Contractor



LLW Construction, Inc.

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com

Erik Devlin <e1devlin@hotmail.com>

Mon, Feb 17, 2025 at 6:05 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: "amberbell000@gmail.com" <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Mike,

This is what we need, This is what we expect.

Goal is to get us back into our home efficiently and effectively the right way.

Updates Monday on what to expect and Friday on what was done and how we are moving forward.

Fair and reasonable expectations do you agree?

We are behind the timeline which is unfortunate but keeping us in the loop on the project is an expectation so that we can plan accordingly. For example in order to get more money we need 50% or more done so I can schedule an inspection with the bank so WE can receive that money. It also gives us time lines on when we can close our lease on our rental and our storage units as well as order appliances and hire movers to get back in. Im pointing this out so we do not need these back and forth emails on what is happening.

Do you agree email seems to be the most effective means of communication so I will press forward with this?

Keep this going Mike , and let me
Know if you need anything !

Erik

Sent from my iPhone

On Feb 17, 2025, at 5:25 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik and Amber,

Here is a brief update for your project on Belcher Dr:

- We received a cabinet shipment for your white kitchen cabinets today – we have them in our storage until we are ready to install.
- The tile installer is ready to begin the tile work, starting with the floor prep tomorrow – it should take a maximum of 3-4 days of prep.
 - We are getting prep materials to the site tonight or tomorrow first thing.
 - The contents that are in the way will be moved to one of the bedrooms – our men will do it first thing in the morning. They will relocate as needed.
- The plumbers will issue a proposal for the master bath plumbing modifications per your conversation with them.
- Shower pan liners, plumbing, and drains installation is completed.
 - Ready for mud bed and tile backer.

- We are ready to hang interior doors – will do this either after the floor prep is complete or after the main floor tile is installed, whichever order keeps things moving faster.

That is all we have today. This should take us through the next 7-10 days. I will submit additional information later in the week as we receive it.

Thanks,

Mike

Michal J. Winiarek

Certified Building Contractor

<image001.jpg>
[Quoted text hidden]





Amber Bell <amberbell000@gmail.com>

Body sprayer quote

1 message

Erik Devlin <e1devlin@hotmail.com>

Fri, Feb 21, 2025 at 9:31 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

I texted this also:

I just reached out to the plumbers and asked what their quote was for body sprayers in the master bathroom. Advised me they sent the quote over to Sharon. They also left me their bosses phone number if I had questions .

What kind of numbers are we talking for the body sprays?

Sent from my iPhone



Amber Bell <amberbell000@gmail.com>

Fwd: Follow up and Bank Inspection

2 messages

Erik Devlin <e1devlin@hotmail.com>

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Sorry I sent that before it was complete.

I need some one at the house between 12-2pm Wednesday. I should be able to be there however if we have workers there that would be helpful.

Please let me know this works for everybody

Thanks!

Erik

Sent from my iPhone

Begin forwarded message:

From: Erik Devlin <e1devlin@hotmail.com>

Date: February 24, 2025 at 11:49:23 AM EST

To: MICHAL WINIAREK <mikew@llwbuild.com>

Subject: Follow up and Bank Inspection

Team,

Sharon thanks for following up on the body sprayers. Looking for 2 body sprayers and a price. Think you said 3 body sprayers \$3700 ish.

Workers are at the house prepping the floors . Whats the idea behind the proflex before the tile is laid ? I sure I could google it but figured Id ask.

Floors to be started this week ? Prep work is looking good so far.

Bank inspection this wednesday.

11:40

5G+



Inspector >

happen to be in the Tampa area
still.

Not today. I'll reach out when I can
about a day next week

Thanks

Today 11:09 AM

Hello, I will be doing a route of
inspections in South Tampa
Wednesday and can arrive at the
home some time between 12-2pm
and be there for about 10 minutes
to do the inspection. Any person
can meet me there to bring me
inside to take photos and I can

give that person a 30 min heads up before I arrive. If there is a way for me to enter the home on my own, that is sufficient and preferred.

If Wednesday doesn't work, I can reach out to you the next time I'm working the area.

Wednesday please and thank you

Deliv

Great see you then



iMessage

Sent from my iPhone

On Feb 21, 2025, at 9:23 AM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Sure - let me know what the inspection schedule is - sooner the better - this stuff always takes some time and these trades are super hungry. They're always sweating me before paint dries. I'm always floating \$50k of our own cash out there between jobs so maintaining steady cashflow is important.

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>
Sent: Friday, February 21, 2025 9:15:32 AM
To: MICHAL WINIAREK <mikew@llwbuild.com>
Subject: Re: Bank Inspection

Yes, 50% or more has to be done to get money.

Is next week fine ?

Sent from my iPhone

On Feb 21, 2025, at 9:09 AM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik,

Could you call for the bank inspection? We will need funds as these guys start burning through the tile work.

Thanks,

Mike

Michal J. Winiarek
Certified Building Contractor

<image001.jpg>

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086
www.LLWbuild.com

MICHAL WINIAREK <mikew@llwbuild.com>

To: Erik Devlin <e1devlin@hotmail.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Mon, Feb 24, 2025 at 12:04 PM

We can make that work

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>
Sent: Monday, February 24, 2025 11:55 AM
To: MICHAL WINIAREK <mikew@llwbuild.com>; Sharon Knight <sharonk@llwbuild.com>; Amber Bell <amberbell000@gmail.com>
Subject: Fwd: Follow up and Bank Inspection

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Re: Payment

1 message

Erik Devlin <e1devlin@hotmail.com>
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>

Thu, Feb 27, 2025 at 6:50 PM

Im flying til midnite tonite. Then flying all
Day Friday Saturday Sunday .

Im on call with the airline so my schedule is unpredictable. This is why I was pushing for the inspection sooner than later
so we would not run into this.

Let me see what I can do tomorrow .

Thanks

Erik
Sent from my iPhone

On Feb 27, 2025, at 6:03 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik,

Could you let me know what you could do for payment? We don't quite know how long the process may
take with the bank inspection and the subsequent steps/entities that have to process whatever they need to
process to release your insurance funds.

Could you wire us 15K tomorrow? Right now the remaining contract balance, without getting into real
financial reconciliation (which we will do) is a tad over \$53K.

Let me know what you could do.

Thanks,

Mike.

Michal J. Winiarek

Certified Building Contractor

<image001.jpg>

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com



Amber Bell <amberbell000@gmail.com>

Paid \$10,000

1 message

Erik Devlin <e1devlin@hotmail.com>

Fri, Feb 28, 2025 at 9:28 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Team,

Wired LLW Construction \$10,000 . This is all we could afford , Spoke to Bank Yesterday , Should have a check next week. As previously stated in emails and texts last two weeks, We need that inspection for money, so we are going in the right direction.

Will be flying till Midnite next two days. Email will be best way to get a hold of me.

Please keep us posted when we receive the tile.

Thanks for your hard work and patience

Erik



Amber Bell <amberbell000@gmail.com>

Tile status ?

3 messages

Erik Devlin <e1devlin@hotmail.com> Mon, Mar 3, 2025 at 8:48 AM
To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

How we looking this week ?

Tiles in ? I thought you said Friday or Monday .

More progress on the bathrooms too ?

Touch base on bank check later in the week.

Sent from my iPhone

Sharon Knight <sharonk@llwbuild.com> Mon, Mar 3, 2025 at 9:59 AM
To: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>

Tile delivery today. Installers meeting me there this afternoon

Get [Outlook for iOS](#)

From: Erik Devlin <e1devlin@hotmail.com>
Sent: Monday, March 3, 2025 8:48:42 AM
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>; Sharon Knight <sharonk@llwbuild.com>
Subject: Tile status ?

[Quoted text hidden]

Erik Devlin <e1devlin@hotmail.com> Mon, Mar 3, 2025 at 1:40 PM
To: Sharon Knight <sharonk@llwbuild.com>
Cc: MICHAL WINIAREK <mikew@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Thank you !
Sent from my iPhone

On Mar 3, 2025, at 9:59 AM, Sharon Knight <sharonk@llwbuild.com> wrote:

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

March 17th updates

5 messages

Erik Devlin <e1devlin@hotmail.com>

Mon, Mar 17, 2025 at 7:17 AM

To: Mike Winiarek <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Team,

How is the tile looking ? We getting bathrooms going as well ?

Where are we at and what is the plan this week. As always we are excited to get back in.

Happy St Patricks Day !

Erik

Sent from my iPhone

> On Mar 3, 2025, at 6:48 AM, Erik Devlin <e1devlin@hotmail.com> wrote:

>

> How we looking this week ?

>

> Tiles in ? I thought you said Friday or Monday .

>

> More progress on the bathrooms too ?

>

>

> Touch base on bank check later in the week.

>

> Sent from my iPhone

Sharon Knight <sharonk@llwbuild.com>

Tue, Mar 18, 2025 at 1:41 PM

To: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>

Hi Erik -

I am working with ProSource to get the additional tiles needed to complete - m Bath - one tile short.... and the main flooring. Tile to be completed this week.

We are waiting on interior doors to come in and will install ASAP. Cabinet install scheduled for next week and tops to follow.

Thank you!

Sharon

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Monday, March 17, 2025 7:17 AM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>; Sharon Knight <sharonk@llwbuild.com>

Subject: March 17th updates

[Quoted text hidden]

Amber Bell <amberbell000@gmail.com>

To: Sharon Knight <sharonk@llwbuild.com>

Cc: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>

Thu, Mar 20, 2025 at 1:06 PM

Team, just sent a text and following up with an email.


- 1) The floor tiles in Liv's bathroom are wrong.
- 2) The corner seems in Livs shower look awful and are not lined up.
- 3) The shower tiles in the master bath are 2 completely different colors. I thought the tiles we picked were both a whitish color.

There is no quality control and this is not acceptable. Please let me know how this will be rectified.

Thanks,



Amber

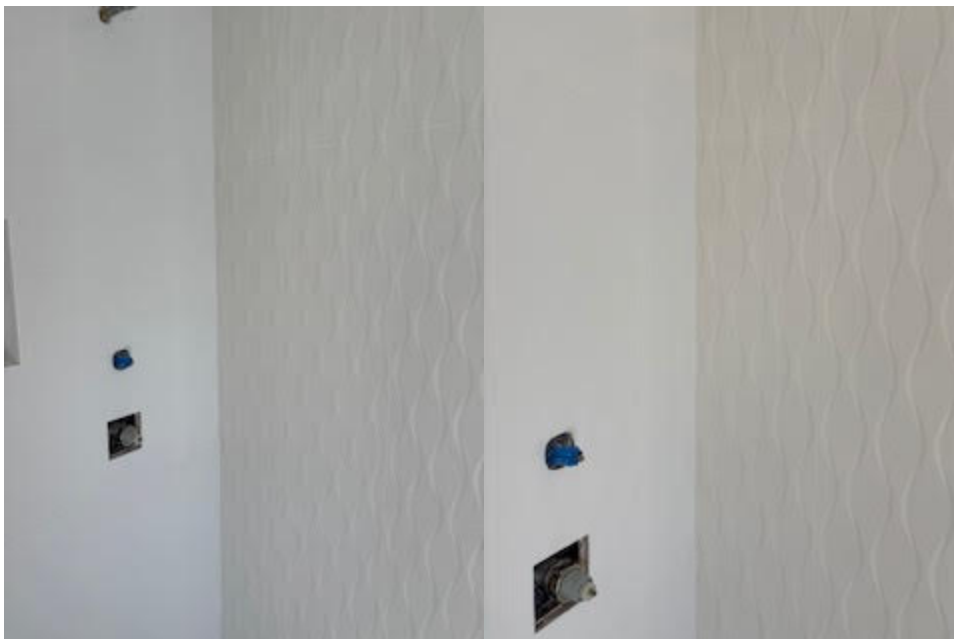



On Mar 18, 2025, at 1:41 PM, Sharon Knight <sharonk@llwbuild.com> wrote:

[Quoted text hidden]

Sharon Knight <sharonk@llwbuild.com>

Thu, Mar 20, 2025 at 2:16 PM

To: Amber Bell <amberbell000@gmail.com>

Cc: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>

Hi Amber-

Following up on our call earlier and keeping everyone in the loop.

I will meet you at the house tomorrow at 10 so we can go over the options for M Bath finish and Liv's bath. See you then!

Thanks,
Sharon

Get [Outlook for iOS](#)

From: Amber Bell <amberbell000@gmail.com>
Sent: Thursday, March 20, 2025 1:06:13 PM
To: Sharon Knight <sharonk@llwbuild.com>
Cc: Erik Devlin <e1devlin@hotmail.com>; MICHAL WINIAREK <mikew@llwbuild.com>
Subject: Re: March 17th updates

[Quoted text hidden]

Amber Bell <amberbell000@gmail.com>
To: Sharon Knight <sharonk@llwbuild.com>
Cc: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>

Thu, Mar 20, 2025 at 5:14 PM

Sounds good. See you then.

Thanks,

Amber Bell
813.335.9891

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Middle Bathroom

3 messages

Erik Devlin <e1devlin@hotmail.com>

Mon, Apr 7, 2025 at 7:04 AM

To: Mike Winiarek <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Team,

The bathroom shower wall is not plumb. It is 63 inches on the floor 64.5 inches at the top. The wall is literally curved just like the drywall was .

Again the workers (Diegos Crew) said that is just how it is. They said the curved wall is why the tile job doesn't look good.

Why does no one communicate this to me?

I had to find this out myself with the Drywall and now I'm having to find it out with the bathroom.

Lets not do this three times like the drywall.

This is unacceptable. The wall needs to be fixed. All the tiles need to be pulled out.

We need to meet with you at the house so you can see this.

Please help me understand why this is happening? I'm trying to let you all do the job you're assigned. However, no one looks over the subcontractors after their work is done. I am the only means of quality assurance to making sure things are done properly

Please tell me how we can fix this? I've asked you in the past if I could help out and you said don't worry we have it, It'd be better if you weren't involved talking directly to the sub contractors. I've tried to stay out of it and every time I stay out of it, there's a problem.

I am beyond disappointed and upset ,every moment something like this happens it's a setback that keep us from getting into our house. We are constantly bleeding money each month for this project.

This needs to be addressed Today.

Sent from my iPhone

MICHAL WINIAREK <mikew@llwbuild.com>

Mon, Apr 7, 2025 at 7:22 AM

To: Erik Devlin <e1devlin@hotmail.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Hi Erik,

I will look at this today. It is the first time I am hearing of this and will see how we can help.

Mike.

Michal J. Winiarek
Certified Building Contractor

Mobile: 813-787-0361
Email: MikeW@LLWbuild.com

Lic.: CBC 1262086
www.LLWbuild.com

[Quoted text hidden]

MICHAL WINIAREK <mikew@llwbuild.com>

Mon, Apr 7, 2025 at 12:59 PM

To: Erik Devlin <e1devlin@hotmail.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Hi Erik,

I asked everyone involved in the tile job about the wall. This bowed wall issue was already identified by Sharon a couple weeks ago and already discussed with the tile installers. They committed to fixing it and have not done yet. This is not new - just hasn't been completed yet.

Mike

Michal J. Winiarek
Certified Building Contractor

Mobile: 813-787-0361
Email: MikeW@LLWbuild.com

Lic.: CBC 1262086
www.LLWbuild.com

-----Original Message-----

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Monday, April 7, 2025 7:04 AM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>; Sharon Knight <sharonk@llwbuild.com>

Subject: Middle Bathroom

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Bathroom 2 plum even walls

1 message

Erik Devlin <e1devlin@hotmail.com>

Tue, Apr 8, 2025 at 11:29 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>

Cc: Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Team,

Per conversation with Mike. Walls in Bathroom number 2 shower need to be level plum walls to include north wall, west wall, south wall. Walls shall be symmetrical on floor and ceiling to ensure and promote smooth installation of tiles.

No tiles shall be re installed until home owners have inspected and confirmed walls meet criteria above. Would recommend Mike or Sharon putting eyes on this before Tile goes back in.

Adhering to this plan will prevent negligence and waste in man hours and materials.

This should all be read as a true/false statement. All criteria above must be true to move forward. Any questions please speak up now.

Thank you for your time and effort!

Erik Devlin

Mike, still need cabinet invoice

Sent from my iPhone



Amber Bell <amberbell000@gmail.com>

Communicate !

1 message

Erik Devlin <e1devlin@hotmail.com>

Sat, Apr 12, 2025 at 9:40 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Diego just called me about the bathroom. He said he needs sharon or Mike to explain this to him on what needs to be done with the bathroom.

Plum walls
Symmetrical walls
All three walls
Must meet this criteria

I got an emergency call last night at 2am because multiple
Family members health were compromised last night

I have not slept and I am in Michigan

This should be handled promptly
Sent from my iPhone



Amber Bell <amberbell000@gmail.com>

Update Needed

3 messages

Amber Bell <amberbell000@gmail.com>

Thu, Apr 17, 2025 at 5:13 PM

To: MICHAL WINIAREK <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, throttl80 <e1devlin@hotmail.com>

Mike / Sharon,

I went by the house this morning and aside from Liv's shower wall having the tile removed, it is clear that no further progress has been made. This lack of movement is unacceptable. We expect updates on the following items by the close of business tomorrow, Friday, April 18th:

- **Cabinets:** We were informed weeks ago that the remaining cabinets (island, laundry room, master bath) were being stored. What is the reason for the delay?
- **Countertops:** Why haven't the countertops been reinstalled on the completed white cabinets?
- **Master Closet:** When will the master closet be rebuilt?
- **Master Bathroom Fixtures (shower and light):** When will these fixtures be reinstalled?
- **Trim Work:** When will the trim work be caulked and painted?
- **Front Bathroom Floor Tile:** When will the grout issues be addressed?
- **Liv's Bathroom Vanity and Fixtures:** Will Sharon be placing the order for these? We sent the selections months ago.
- **AC Units:** Are you handling these? If so, when will they be ordered?
- **Estimated Completion Date:** The last estimated completion date we received was February 21st. We have asked for an update on this several times and expect one to be provided with this list of items.

Our frustration and disappointment with this entire process have reached a critical point. Despite our continued efforts to set expectations, we feel they are only disregarded. We need immediate action and communication moving forward.

Thanks,

Amber

MICHAL WINIAREK <mikew@llwbuild.com>

Mon, Apr 21, 2025 at 8:50 AM

To: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>, throttl80 <e1devlin@hotmail.com>

Hello

I will issue a better update a bit later today but wanted to get the most urgent item addressed

I met with Miguel this morning in the middle bathroom and we have a plan on how to make that perfect, the tile guy still complained about some irregularity with the furring strips, however, he used the torpedo level to demonstrate his point. That is completely Unacceptable and frankly stupid to use the torpedo level to try to gauge a quality of anything. Short levels are used to set small things not demonstrate an entire wall

Miguel will apply one more layer of 1/4 inch furring strips on top of existing furring strips but stop short of the rubber membrane and then they will have a nice solid surface to put the underlayment board on. The rest will be up to them to make the tile look good. we believe this gives them the best possible chance to make the shower as perfect as it can be.

Michal Winiarek

LLW Construction Inc
(813) 787-0361

From: Amber Bell <amberbell000@gmail.com>
Sent: Thursday, April 17, 2025 5:15 PM
To: MICHAL WINIAREK <mikew@llwbuild.com>; Sharon Knight <sharonk@llwbuild.com>; throttl80 <e1devlin@hotmail.com>
Subject: Update Needed

[Quoted text hidden]

Erik Devlin <e1devlin@hotmail.com>
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Tue, Apr 22, 2025 at 7:26 AM

This was the last update I see on the house:

Hi Erik and Amber,

We just revised the project schedule and here is what we can expect moving forward:

- Walls corrected and primed; stone picked up; plumbing modifications completed; tile prep and backer board installed by 1/17
- Doors and trim installed; paint 1 completed by 1/28
- Tile installed and cabinets delivered by 2/7
- Cabinets and counters installed; locks, hardware, shelving installed by 2/14
- Backsplashes installed; trim plumbing and electric completed; final clean performed by 2/20
- Home Delivery 2/21

Sent from my iPhone

On Apr 21, 2025, at 8:50 AM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Updates please and Thank you

1 message

Erik Devlin <e1devlin@hotmail.com>

Mon, Apr 21, 2025 at 6:25 AM

To: MICHAL WINIAREK <mikew@llwbuild.com>

Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Please respond , Thanks !

Sent from my iPhone

On Feb 4, 2025, at 1:46 PM, Erik Devlin <e1devlin@hotmail.com> wrote:

Hey Mike,

Hope you are ok. I text yesterday and today as well as called yesterday and today. Goes right to voicemail looks like your phone is in Do not disturb.

Please let me know you are good

Thanks !!

Erik

Sent from my iPhone

On Jan 10, 2025, at 6:10 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

Hi Erik and Amber,

We just revised the project schedule and here is what we can expect moving forward:

- Walls corrected and primed; stone picked up; plumbing modifications completed; tile prep and backer board installed by 1/17
- Doors and trim installed; paint 1 completed by 1/28
- Tile installed and cabinets delivered by 2/7
- Cabinets and counters installed; locks, hardware, shelving installed by 2/14
- Backsplashes installed; trim plumbing and electric completed; final clean performed by 2/20
- Home Delivery 2/21

The above is a condensed plan – we have a much more detailed project schedule that we manage internally. Thank you for being patient so far.

Have great weekend.

Mike.

Michal J. Winiarek

Certified Building Contractor

<image001.jpg>

Mobile: 813-787-0361

Email: MikeW@LLWbuild.com

Lic.: CBC 1262086

www.LLWbuild.com

<image001.jpg>



Amber Bell <amberbell000@gmail.com>

Update Pending

1 message

MICHAL WINIAREK <mikew@llwbuild.com>

Tue, Apr 22, 2025 at 5:00 PM

To: Erik Devlin <e1devlin@hotmail.com>, Amber Bell <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>

Hi Erik and Amber

I realize you are waiting for a more detailed update and I really appreciate your patience so far. I have been spread really thin last couple of days and have not been able to run down all the information to adequately update y'all and answer the questions. I do not want to feed you a bunch of lines and issue something that is just going to be a wild guess.

I really want to bring the whole job to a close within the next 3 week or so, but I still need some more information to be able to accurately predict all the pieces .

I ask that you allow me 1-2 more days and I will have a game plan for completion put together.

In the meantime Sharon and I are working to get the bathroom issue resolved - the wallboard went up and we need to check it all to make sure we can continue with reinstalling the tile that Sharon can order right away.

Thanks

Mike

Michal Winiarek
LLW Construction Inc
(813) 787-0361



Amber Bell <amberbell000@gmail.com>

Belcher Update 4.25.25

3 messages

MICHAL WINIAREK <mikew@llwbuild.com>

Fri, Apr 25, 2025 at 12:12 PM

To: Erik Devlin <e1devlin@hotmail.com>, Amber Bell <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>

Hi Erik and Amber,

Thanks for being so patient. Here is the most recent update.

- **Cabinets:** We were informed weeks ago that the remaining cabinets (island, laundry room, master bath) were being stored. What is the reason for the delay?
 - *I do not have an explanation for this – we can get the cabinets installed and counters placed in the next 14 – 20 days*
- **Countertops:** Why haven't the countertops been reinstalled on the completed white cabinets?
 - *All the counters will be installed at the same time – 14-20 days*
- **Master Closet:** When will the master closet be rebuilt? –
 - *This coming week*
- **Master Bathroom Fixtures (shower and light):** When will these fixtures be reinstalled?
 - *This coming week*
- **Trim Work:** When will the trim work be caulked and painted?
 - *This coming week*
- **Front Bathroom Floor Tile:** When will the grout issues be addressed? –
 - *1-2 weeks – need to get it scheduled monday*
- **Liv's Bathroom Vanity and Fixtures:** Will Sharon be placing the order for these? We sent the selections months ago.
 - *Yes – now that the tile will be resolved this coming week, we can schedule the trim plumbing. **Please check (if you have not already) if you are OK with the backer board. The sub is squirming pretty badly and although my initial feeling is not to release a dime to them until it is all 100% done and good, we may have to pay them a few bucks and still retain an amount to keep them motivated to finish. I may need you to give them a check directly(will come off our final balance) but only if you approve.***
- **AC Units:** Are you handling these? If so, when will they be ordered?
 - *The Exactimate only addressed the air handlers – I believe that was a mistake and the ac condensers should have been replaced. We have 2 options – Option 1 is we can get the condensers replaced (we believe the handlers are Ok). Option 2 is you can handle the AC work and we give you a credit of \$5,252.56. We can get the work done in the next 10 days.*
- **Estimated Completion Date:** The last estimated completion date we received was February 21st. We have asked for an update on this several times and expect one to be provided with this list of items.
 - *Our new target completion is no later than 5/19*

We will have men at your place several days next week and we really want to get the project wrapped up. I will give you another update by Tuesday afternoon as we progress.

Thanks,

Mike

Erik Devlin <e1devlin@hotmail.com>
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Mon, May 5, 2025 at 8:52 AM

Updates ??

Thanks !

Sent from my iPhone

On Apr 25, 2025, at 12:12 PM, MICHAL WINIAREK <mikew@llwbuild.com> wrote:

[Quoted text hidden]

Erik Devlin <e1devlin@hotmail.com>
To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>
Cc: Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Sun, May 11, 2025 at 9:39 AM

Updates ?

Thanks !
Sent from my iPhone

Begin forwarded message:

From: Erik Devlin <e1devlin@hotmail.com>
Date: May 5, 2025 at 8:53:00 AM EDT
To: MICHAL WINIAREK <mikew@llwbuild.com>
Cc: Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>
Subject: Re: Belcher Update 4.25.25

Updates ??

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Responses need for backsplash tiles

2 messages

Erik Devlin <e1devlin@hotmail.com>

Tue, Apr 29, 2025 at 8:21 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

From

Ambers text yesterday

We agreed we need a response the day questions are asked even if the response is "we are busy"

Please do not disrespect my wife

I know Erik and Mike discussed the kitchen tile backsplash this morning. Are you guys picking this tile or are we?
Sent from my iPhone

MICHAL WINIAREK <mikew@llwbuild.com>

Tue, Apr 29, 2025 at 1:43 PM

To: Erik Devlin <e1devlin@hotmail.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Hi Amber

Go ahead and pick up the tile. We would need approximately 65 square feet. I can have a man help load and transport if we know when you'd go and get it.

Thanks

Mike

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Tuesday, April 29, 2025 8:21 AM

To: MICHAL WINIAREK <mikew@llwbuild.com>; Sharon Knight <sharonk@llwbuild.com>; Amber Bell <amberbell000@gmail.com>

Subject: Responses need for backsplash tiles

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Belcher update

1 message

MICHAL WINIAREK <mikew@llwbuild.com>

Tue, May 13, 2025 at 7:30 AM

To: Erik Devlin <e1devlin@hotmail.com>, Amber Bell <amberbell000@gmail.com>, Sharon Knight <sharonk@llwbuild.com>

Hi Folks

Our guys will be heading to your project today and paint will resume. We should be getting close being able to pick up the replacement wall tile as well so we can wrap up that part of it.

Michal Winiarek
LLW Construction Inc
(813) 787-0361



Amber Bell <amberbell000@gmail.com>

Status

4 messages

Erik Devlin <e1devlin@hotmail.com>

Mon, Mar 24, 2025 at 11:58 AM

To: "Mike Winiarek (contractor)" <mikew@llwbuild.com>, Sharon Knight <sharonk@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Where we at gang ?

Sharon did you get the correct tiles for Livs bathroom floor ?

I know amber and You spoke about that last week.

Where are we at with the tile
For the front two bedrooms ?

Are we putting in Cabinets this week ?

do we have a delivery date in mind?

initially we were projected 4 to 6 weeks from
Date of signing to take us to January. Then projected February 21. Just looking for something realistic I understand how things can get busy but anything you can do to give us a projected realistic date will help us get back to normalcy is greatly appreciated.
Sent from my iPhone

Sharon Knight <sharonk@llwbuild.com>

Mon, Mar 24, 2025 at 2:41 PM

To: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Hi -

I met with the tile installers on Friday. They are going re-work the corners and tile below valve in Liv's bath.

The floor material for Liv's bath is on the way from Atlanta. ETA: Wednesday and the installer will complete remaining tile work.

Following up on door material delivery. Should have this week.

Lots of moving pieces and hope to have clearer answers in the next couple days.

Thanks,
Sharon

LLW Construction, Inc.

Get [Outlook for iOS](#)

From: Erik Devlin <e1devlin@hotmail.com>

Sent: Monday, March 24, 2025 11:58:12 AM

To: MICHAL WINIAREK <mikew@llwbuild.com>; Sharon Knight <sharonk@llwbuild.com>; Amber Bell <amberbell000@gmail.com>

Subject: Status

[Quoted text hidden]

Amber Bell <amberbell000@gmail.com>

Fri, Mar 28, 2025 at 11:54 AM

To: Sharon Knight <sharonk@llwbuild.com>

Cc: Erik Devlin <e1devlin@hotmail.com>, MICHAL WINIAREK <mikew@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Team,

Please provide an update on where we are with the tile, timeframe for tile mistakes in Liv's bathroom to be corrected, what progress was made or accomplished this week, and what the plan is for next week.

We're still waiting on a realistic timeline for project completion needed for planning purposes on our end.

Please advise.

Amber Bell
813.335.9891

[Quoted text hidden]

Erik Devlin <e1devlin@hotmail.com>

Mon, Mar 31, 2025 at 3:41 PM

To: Amber Bell <amberbell000@gmail.com>

Cc: Sharon Knight <sharonk@llwbuild.com>, MICHAL WINIAREK <mikew@llwbuild.com>, Amber Bell <amberbell000@gmail.com>

Hey guys, AMBER and I just stopped by the house about 3:30 PM. Looks like they're pushing forward with cabinets. The cabinets look just like our old ones so far so good on the cabinets. Saw there was some tiles for Liv's bathroom floor. As well as some tiles for her actual bathroom shower . Did not see any tiles to finish off the front two rooms. Where are we at with the tiles for the front two rooms?

Just tried to call Mike went to voicemail.

MONDAY last week Sharon said she would have more information by Wednesday.

We waited until Friday to reach out.

There was no response to AMBER's email on Friday.

Just trying to see where we're at with everything.

I'll shoot you guys an email with all the details of this text message as well.

Mike- invoice or equivalent for cost of Cabinets. Cost of cabinets only ,not cost of install

Mike- estimate for window replacement
What we talked about last week.

Sent from my iPhone

On Mar 28, 2025, at 11:55 AM, Amber Bell <amberbell000@gmail.com> wrote:

[Quoted text hidden]



Amber Bell <amberbell000@gmail.com>

Fw: Looking to help

1 message

Erik Devlin <e1devlin@hotmail.com>
To: Amber Bell <amberbell000@gmail.com>

Wed, Jun 4, 2025 at 7:03 PM

From: MICHAL WINIAREK <mikew@llwbuild.com>
Sent: Wednesday, June 4, 2025 1:21 PM
To: Erik Devlin <e1devlin@hotmail.com>
Subject: Re: Looking to help

Hi Erik

We can get the guys to do the cabinet work

I have the tile guys who can get the tile work done as soon as you're ready

As far as payment, let's see what you can do - I'm open to chunking it up, but we will need something as I can't get people to be effective without paying them. Here to help and I'll flex as much as I can to help you get this to the finish line.

Thanks

Mike

Michal Winiarek
LLW Construction Inc
(813) 787-0361

From: Erik Devlin <e1devlin@hotmail.com>
Sent: Wednesday, June 4, 2025 8:34 AM
To: MICHAL WINIAREK <mikew@llwbuild.com>
Subject: Looking to help

Mike,

I am getting the Air conditioning done both in the front and back of the house. I am ordering the island cabinets for the kitchen, the vanity for the Master Bath, and the cabinets for the Laundry room. I need you to have your guys put together the cabinets and install them.

I checked the measurements for the Laundry room and it was off by 4 inches. Im showing 96 inches wall to wall . You had it at 100 inches. I re measured the master bath Vanity and that was correct. I can not measure the island because it is gone. Please tell me with some degree of certainty that is correct.

Cabinets should be here next week if you can confirm this.

Also we need to finish that shower. I can order the tiles and pay for them , I need your guys to finish this.

Once shower is complete to our satisfaction and cabinets and backsplash maybe we can get some more money. Or we can pay per job. open to ideas or suggestions.

Sent from my iPhone
